ID	Task Name	Duration	Work	Start	Finish
1	**Hardboard Phase 3**	**14.85 wks**	**594 hrs**	**Mon 5/18/15**	**Fri 9/18/15**
2	**Design documents**	**1.75 wks**	**70 hrs**	**Mon 5/18/15**	**Fri 6/12/15**
3	Use cases	30 hrs	30 hrs	Mon 5/18/15	Fri 5/29/15
4	Sequence Diagrams	30 hrs	30 hrs	Sat 5/30/15	Sun 6/7/15
5	Class Diagrams	10 hrs	10 hrs	Mon 6/8/15	Fri 6/12/15
6	**Production Schedule**	**2.28 wks**	**91 hrs**	**Mon 6/15/15**	**Tue 6/30/15**
7	Add press shift configuration	10 hrs	10 hrs	Mon 6/15/15	Tue 6/16/15
8	**Production Window**	**0.38 wks**	**15 hrs**	**Tue 6/16/15**	**Thu 6/18/15**
9	Create controls	15 hrs	15 hrs	Tue 6/16/15	Thu 6/18/15
10	**Press configuration**	**1.15 wks**	**46 hrs**	**Thu 6/18/15**	**Thu 6/25/15**
11	Schedule pait trial (Manual or selected)	8 hrs	8 hrs	Thu 6/18/15	Fri 6/19/15
12	Set max number of plate changes per week	2 hrs	2 hrs	Fri 6/19/15	Fri 6/19/15
13	Set day(s) of week plate changes may happen	4 hrs	4 hrs	Fri 6/19/15	Fri 6/19/15

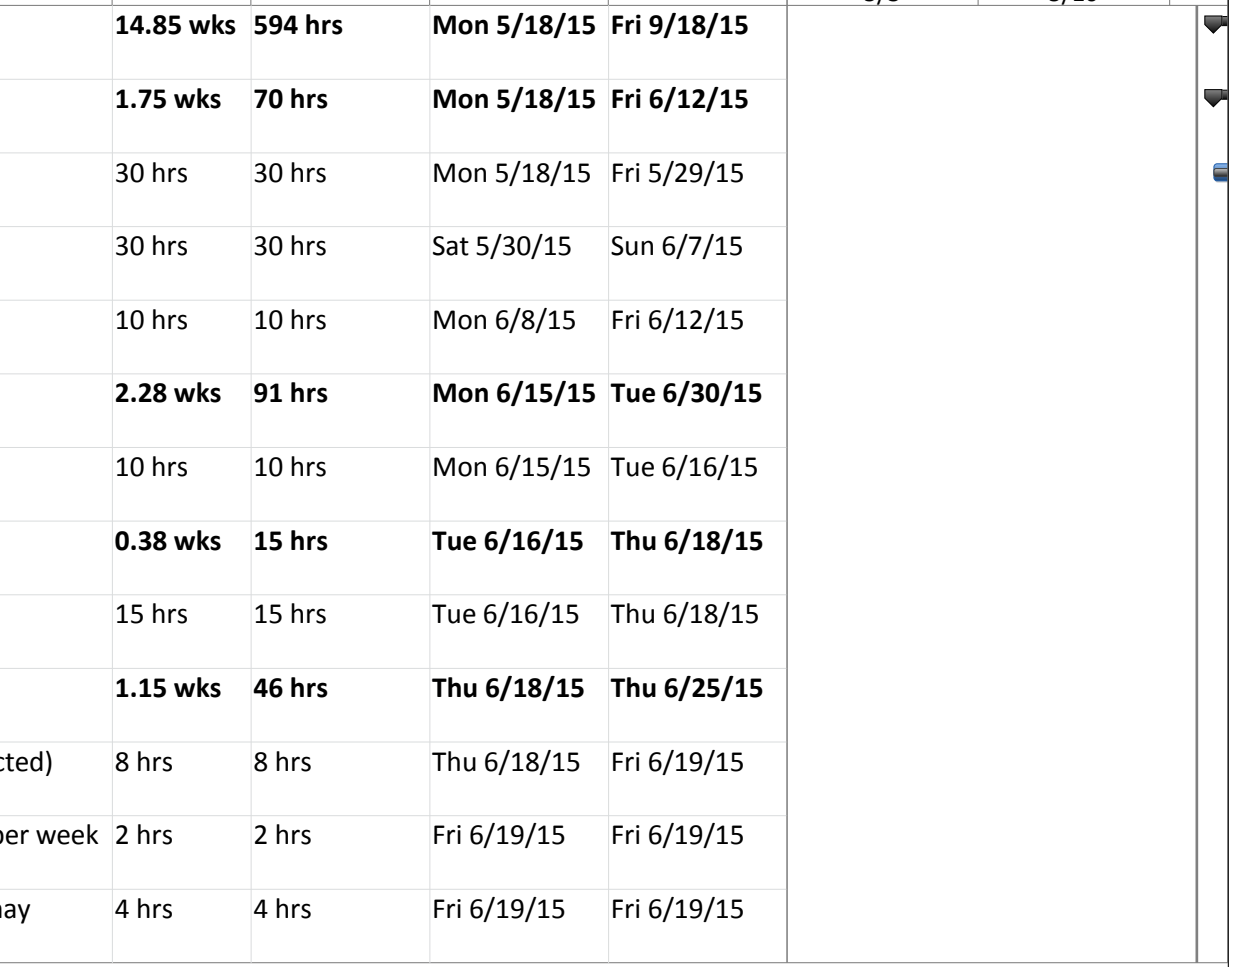

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Deadline
External Tasks	Duration-only	Progress

ID	Task Name	Duration	Work	Start	Finish
14	Plate configuration manual editing	20 hrs	20 hrs	Fri 6/19/15	Wed 6/24/15
15	Rough item list to run	12 hrs	12 hrs	Wed 6/24/15	Thu 6/25/15
16	Testing	20 hrs	20 hrs	Thu 6/25/15	Tue 6/30/15
17	**Update Coating Schedule**	**3.83 wks**	**153 hrs**	**Tue 6/30/15**	**Mon 7/27/15**
18	Running totals of commonly used WiP items	30 hrs	30 hrs	Tue 6/30/15	Mon 7/6/15
19	Schedule paint trial (Manual or selected item)	10 hrs	10 hrs	Mon 7/6/15	Tue 7/7/15
20	Add production time option for schedule in place of units	20 hrs	20 hrs	Tue 7/7/15	Thu 7/9/15
21	Testing	15 hrs	15 hrs	Thu 7/9/15	Mon 7/13/15
22	**Warehouse Tracking**	**1 wk**	**40 hrs**	**Mon 7/13/15**	**Mon 7/20/15**
23	Auto tracking of WiP inventory from estimated production	20 hrs	20 hrs	Mon 7/13/15	Thu 7/16/15
24	Marking warehouse stock to be purged	10 hrs	10 hrs	Thu 7/16/15	Fri 7/17/15
25	Testing	10 hrs	10 hrs	Fri 7/17/15	Mon 7/20/15
26	**Production**	**0.95 wks**	**38 hrs**	**Mon 7/20/15**	**Mon 7/27/15**

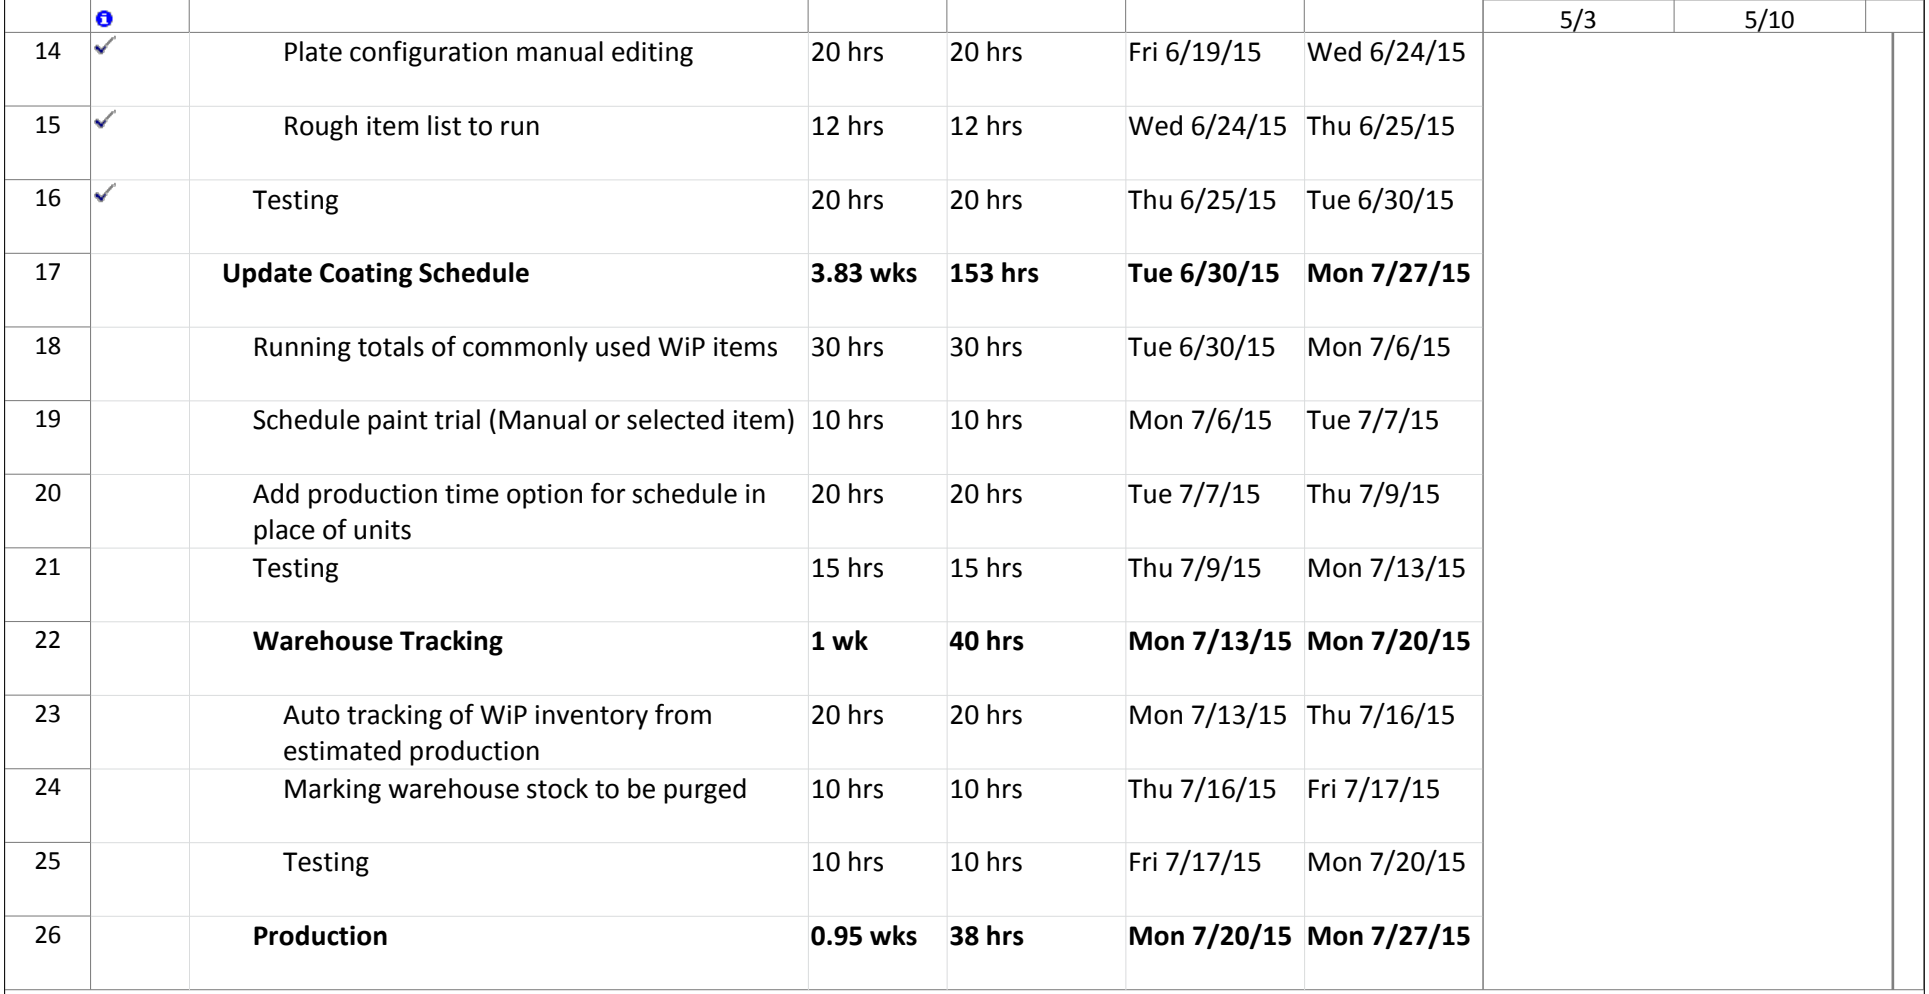

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

ID	Task Name	Duration	Work	Start	Finish
27	Efficiency tracking from standards	20 hrs	20 hrs	Mon 7/20/15	Thu 7/23/15
28	Set machine conflicts	10 hrs	10 hrs	Thu 7/23/15	Fri 7/24/15
29	Testing	8 hrs	8 hrs	Fri 7/24/15	Mon 7/27/15
30	**Update LumberTrack interface**	**0.73 wks**	**29 hrs**	**Mon 7/27/15**	**Fri 7/31/15**
31	Write nightly exports	15 hrs	15 hrs	Mon 7/27/15	Wed 7/29/15
32	Update products to use new product code and dimentions	8 hrs	8 hrs	Wed 7/29/15	Thu 7/30/15
33	Testing	6 hrs	6 hrs	Thu 7/30/15	Fri 7/31/15
34	**Schedule Generation**	**2.95 wks**	**118 hrs**	**Fri 7/31/15**	**Wed 8/26/15**
35	**Priority setting of the following values:**	**2.2 wks**	**88 hrs**	**Fri 7/31/15**	**Fri 8/21/15**
36	Sales prediction	6 hrs	6 hrs	Fri 7/31/15	Fri 7/31/15
37	Shake texture only on Friday	8 hrs	8 hrs	Fri 7/31/15	Mon 8/3/15
38	10 day turnover on new orders	20 hrs	20 hrs	Mon 8/3/15	Thu 8/6/15
39	Items should be made in decreasing width	8 hrs	8 hrs	Thu 8/6/15	Thu 8/13/15

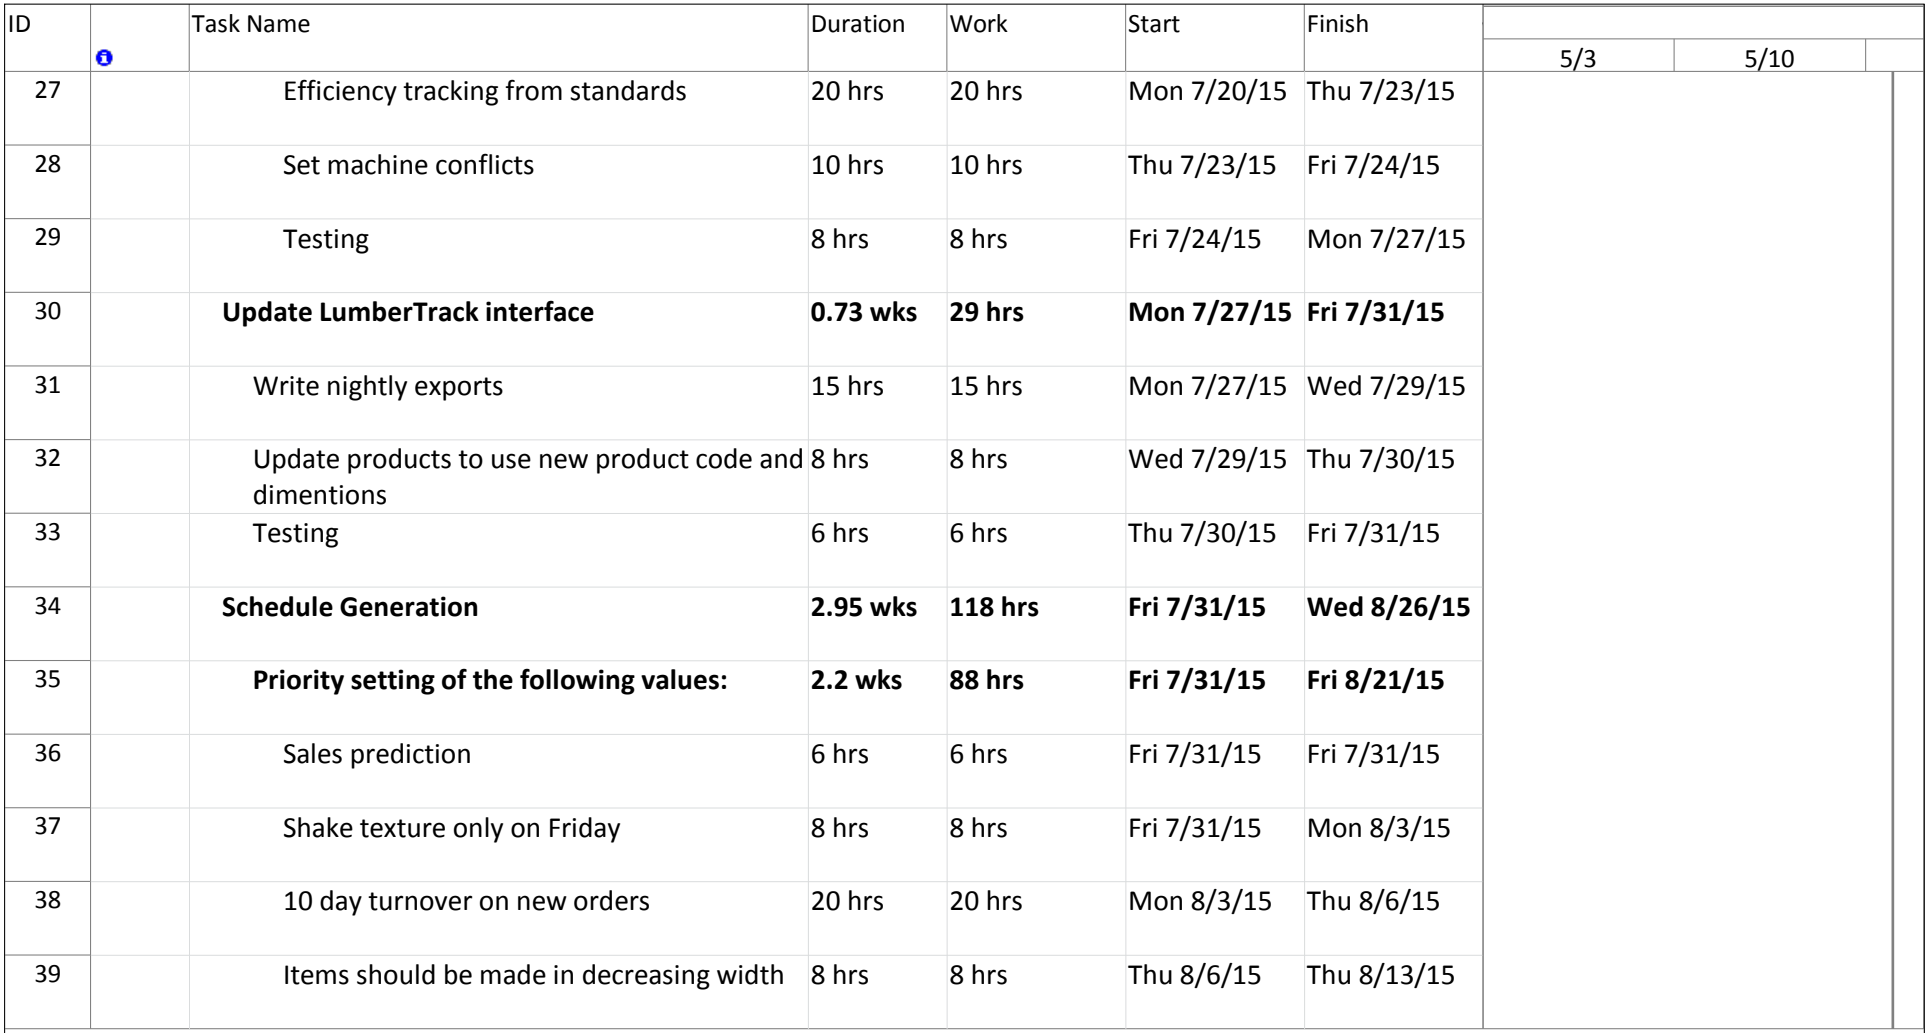

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress

ID	Task Name	Duration	Work	Start	Finish
40	Run unprimed before primed	15 hrs	15 hrs	Thu 8/13/15	Mon 8/17/15
41	Lam line is not run with first pass	15 hrs	15 hrs	Mon 8/17/15	Wed 8/19/15
42	Waste is kept within minimum and maximum values	8 hrs	8 hrs	Wed 8/19/15	Thu 8/20/15
43	Prioritize WiP item use that are marked "pur	8 hrs	8 hrs	Thu 8/20/15	Fri 8/21/15
44	Testing	30 hrs	30 hrs	Fri 8/21/15	Wed 8/26/15
45	**Program Manual**	**3.33 wks**	**133 hrs**	**Wed 8/26/15**	**Fri 9/18/15**
46	**Scope indentification**	**0.25 wks**	**10 hrs**	**Wed 8/26/15**	**Fri 8/28/15**
47	Identify tasks that the user will perform	10 hrs	10 hrs	Wed 8/26/15	Fri 8/28/15
48	**Content**	**2.63 wks**	**90 hrs**	**Mon 8/31/15**	**Thu 9/17/15**
49	Rough draft	60 hrs	60 hrs	Mon 8/31/15	Wed 9/9/15
50	Final document revision	30 hrs	30 hrs	Fri 9/11/15	Thu 9/17/15
51	**Images**	**0.38 wks**	**15 hrs**	**Wed 9/9/15**	**Fri 9/11/15**
52	Capture/Editing	15 hrs	15 hrs	Wed 9/9/15	Fri 9/11/15

5/3 5/10

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task	External Milestone	Manual Summary Rollup	
Split	Inactive Task	Manual Summary	
Milestone	Inactive Milestone	Start-only	
Summary	Inactive Summary	Finish-only	
Project Summary	Manual Task	Deadline	
External Tasks	Duration-only	Progress	

ID	Task Name	Duration	Work	Start	Finish
53	**Layout**	**3.08 wks**	**18 hrs**	**Fri 8/28/15**	**Fri 9/18/15**
54	Template creation	10 hrs	10 hrs	Fri 8/28/15	Mon 8/31/15
55	Revision	8 hrs	8 hrs	Thu 9/17/15	Fri 9/18/15

5/3 5/10

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

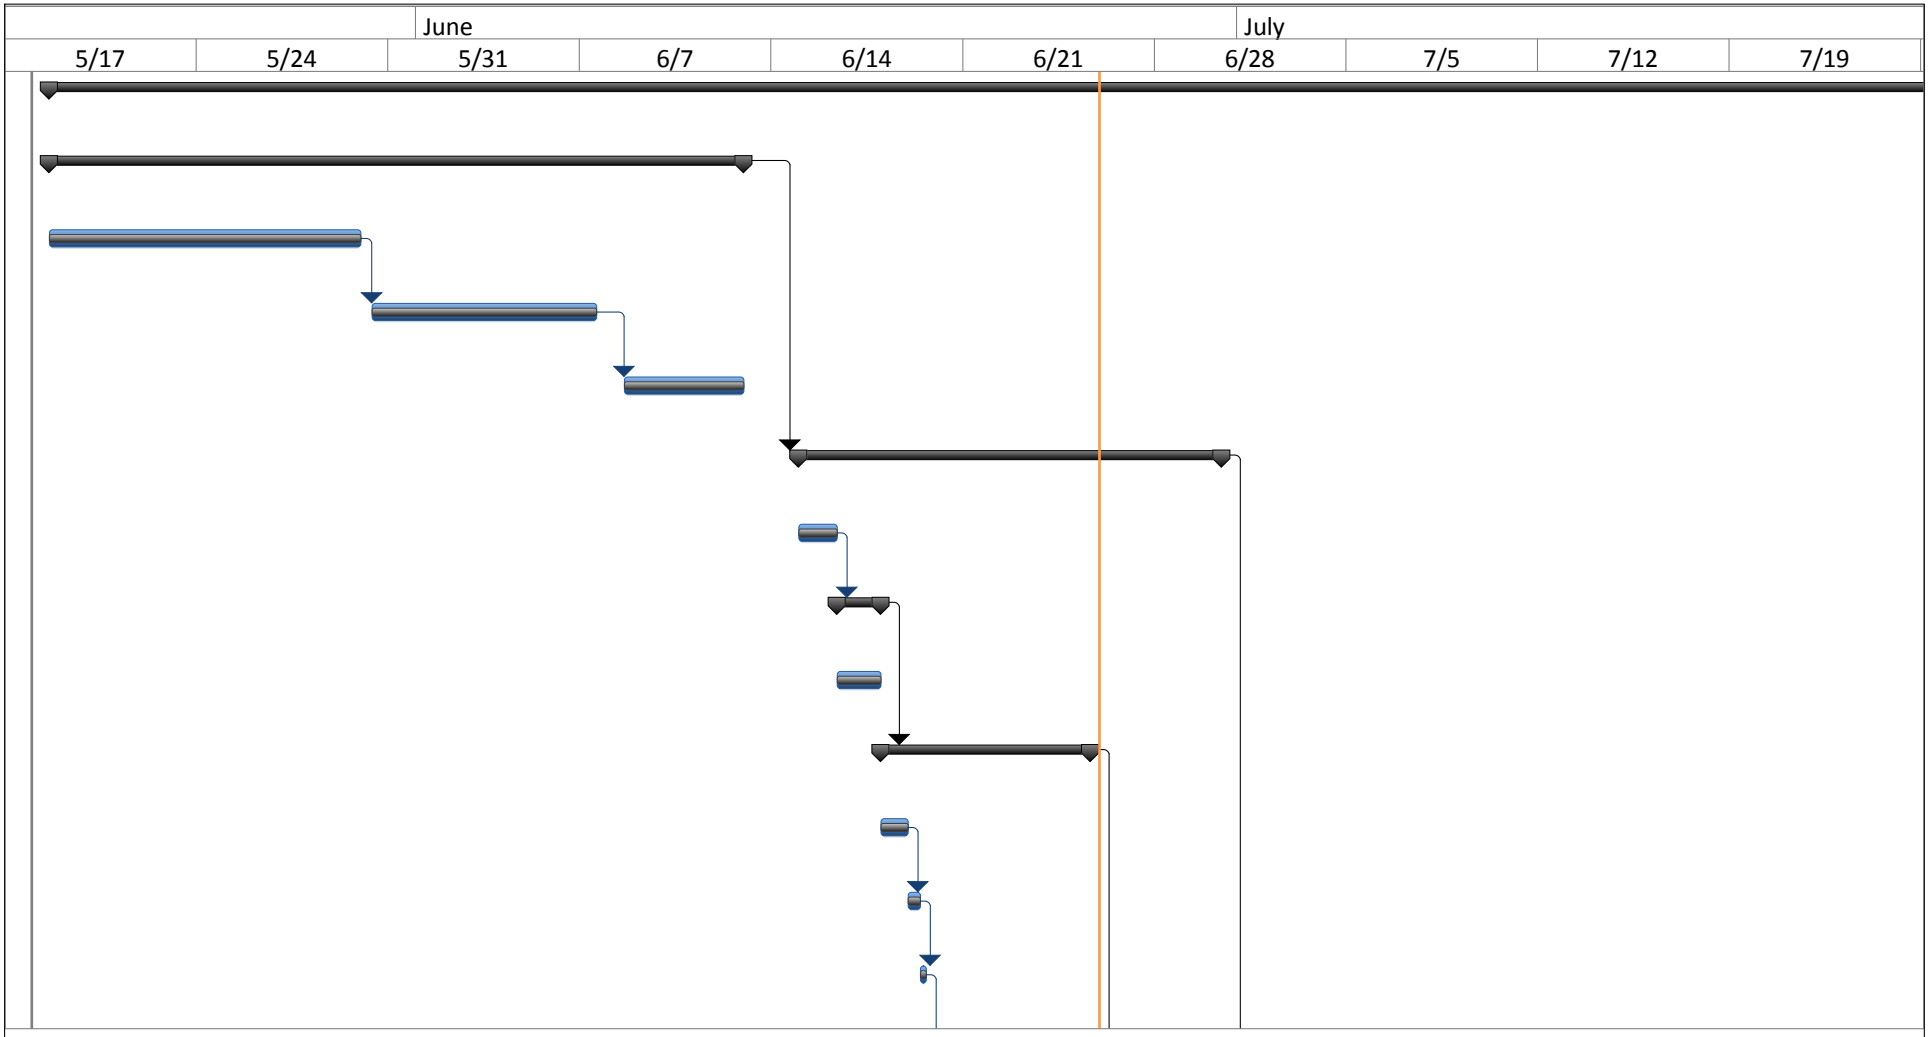

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

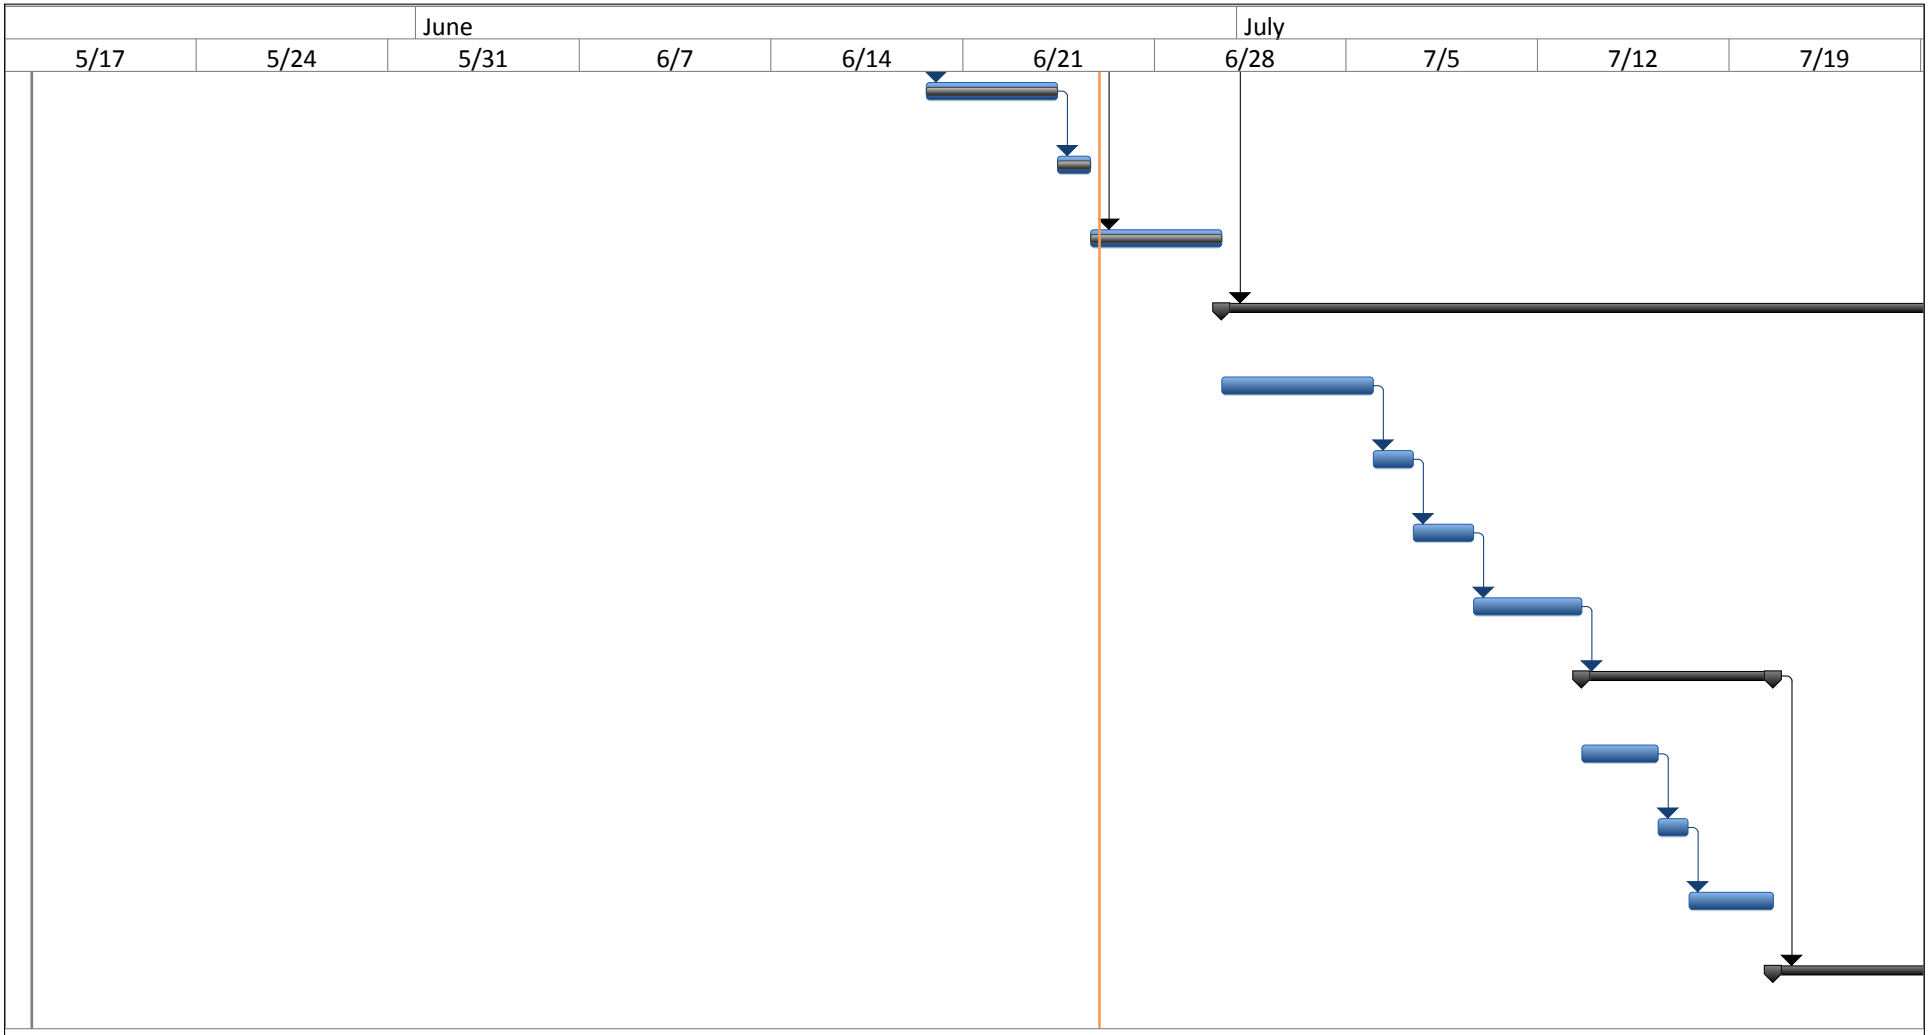

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

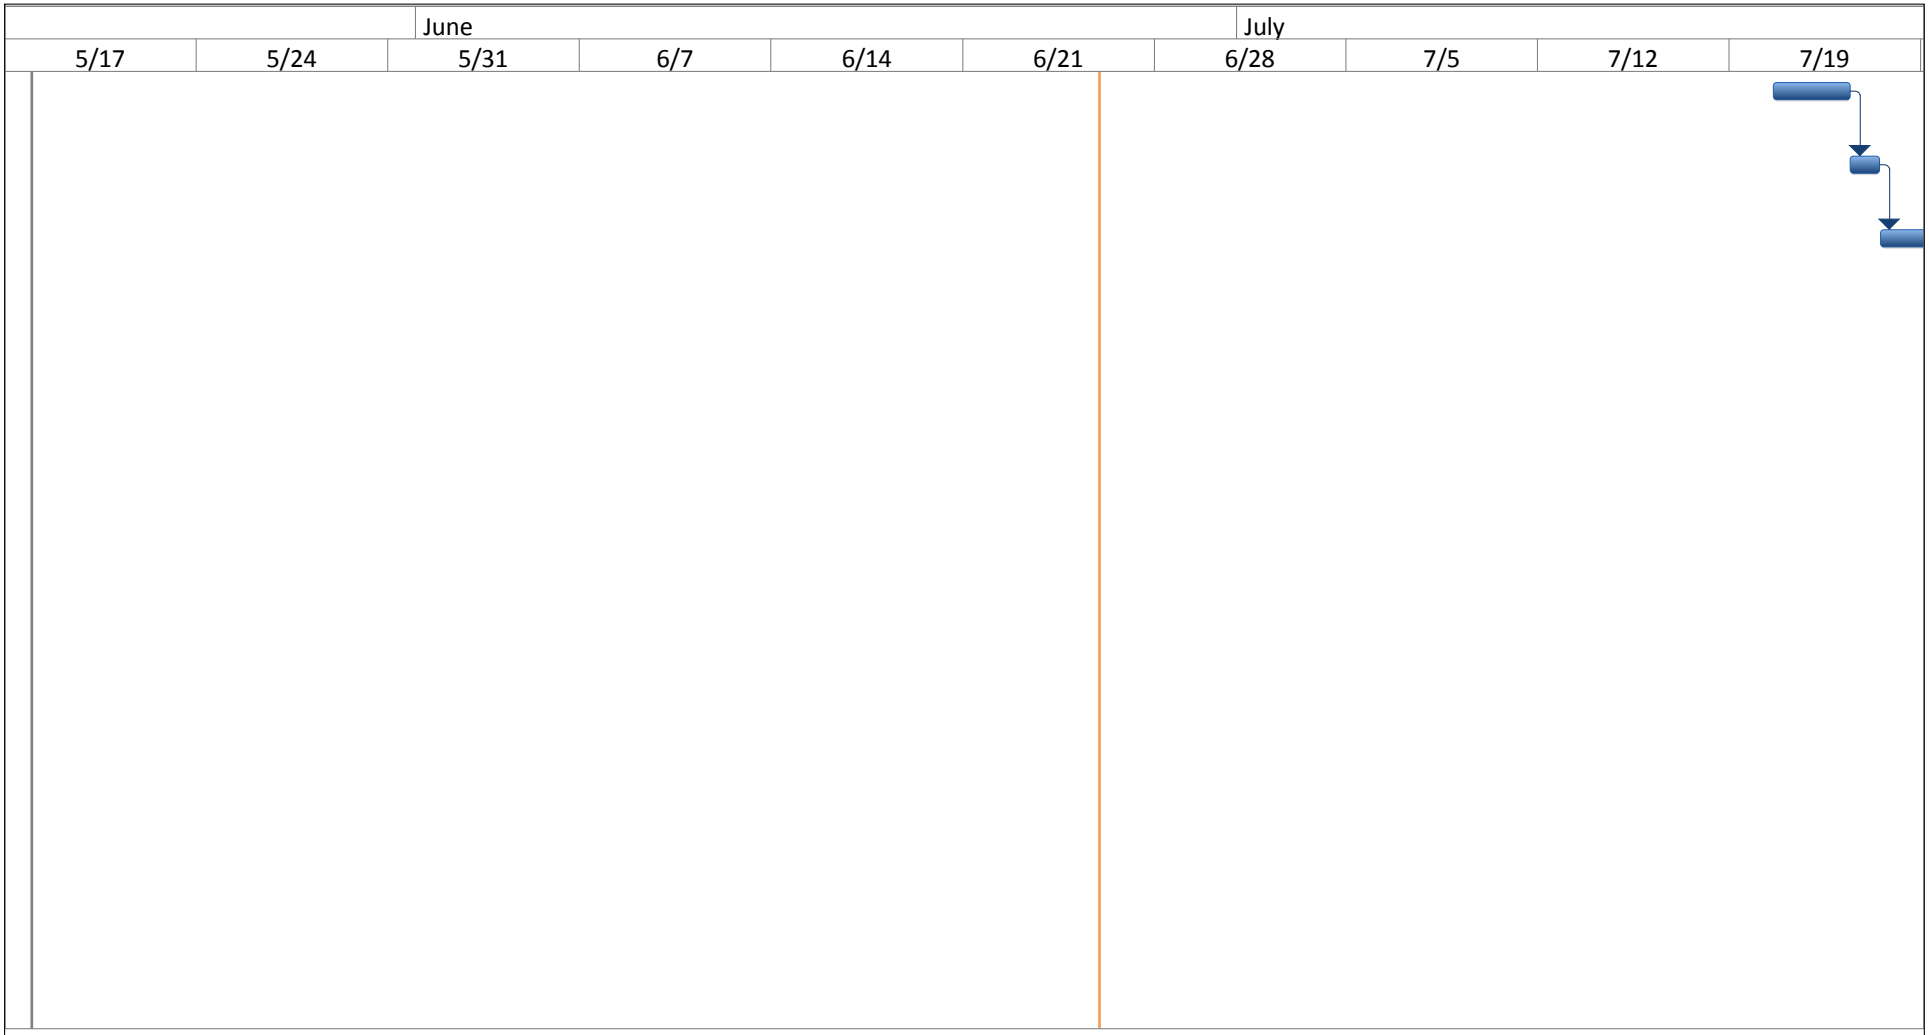

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

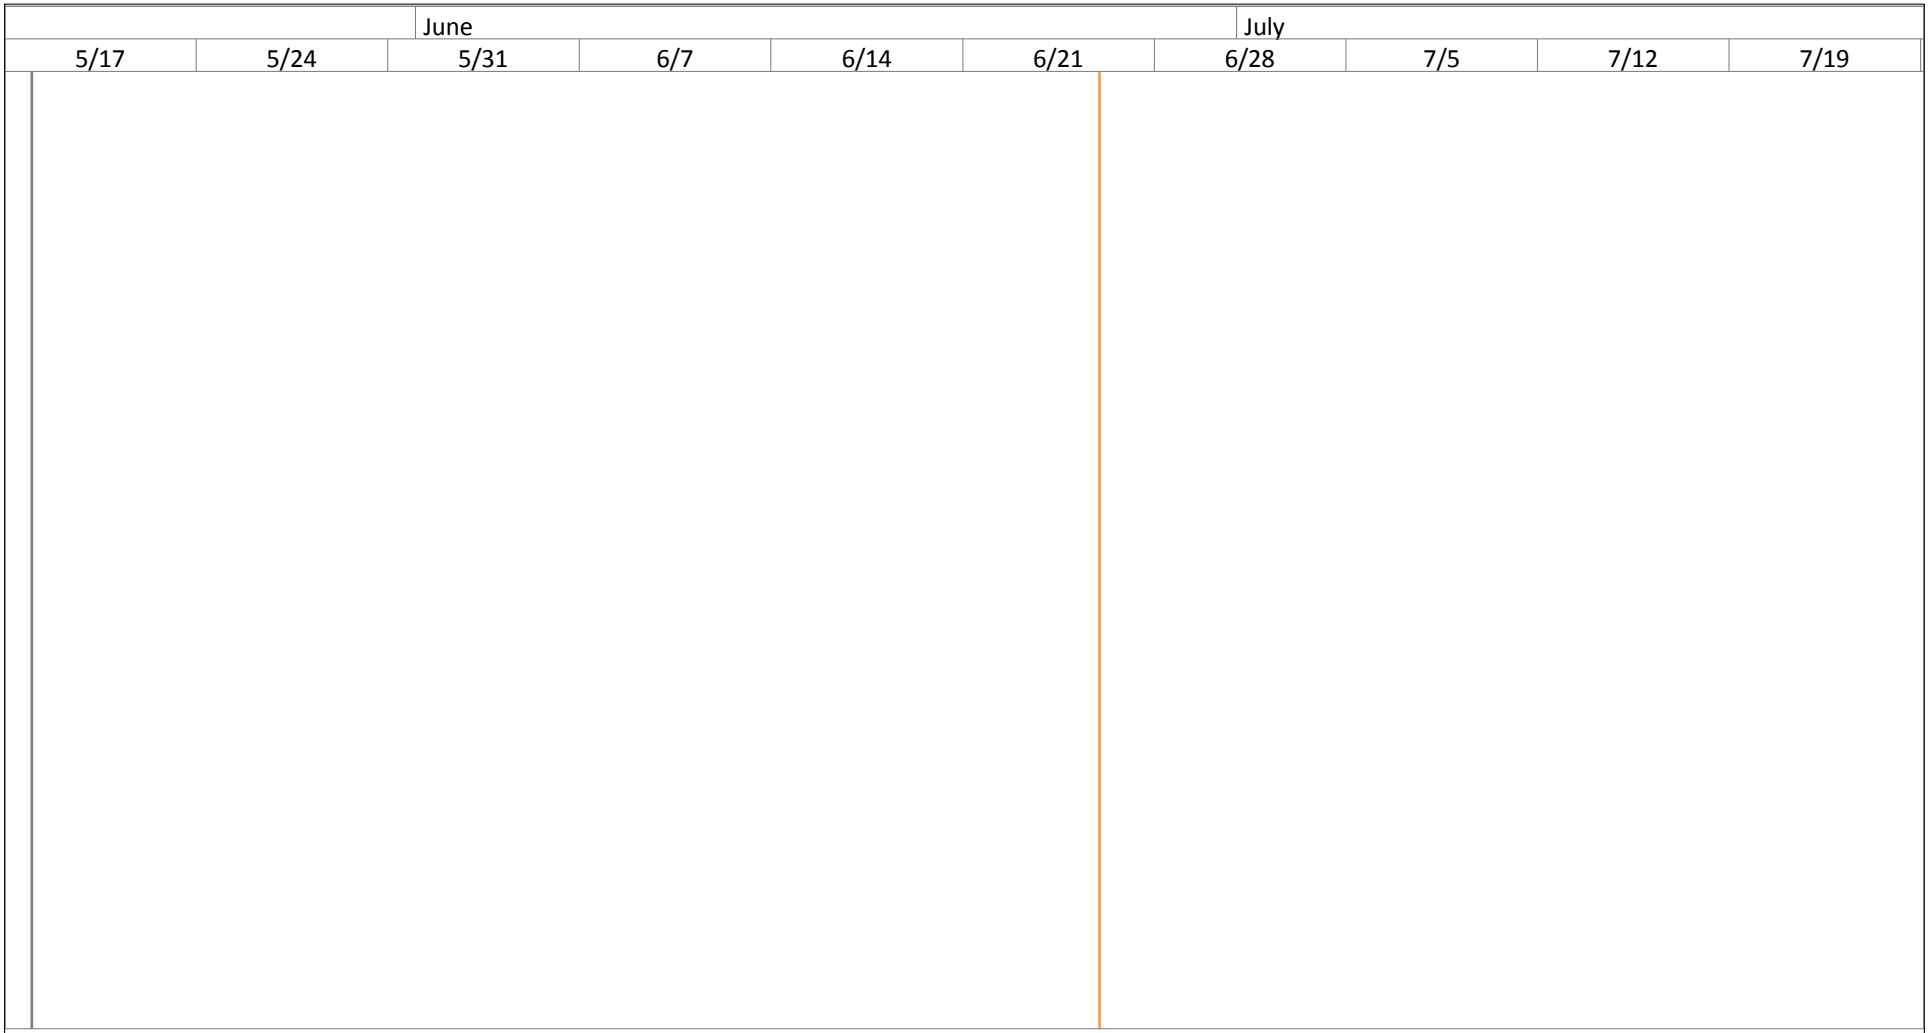

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

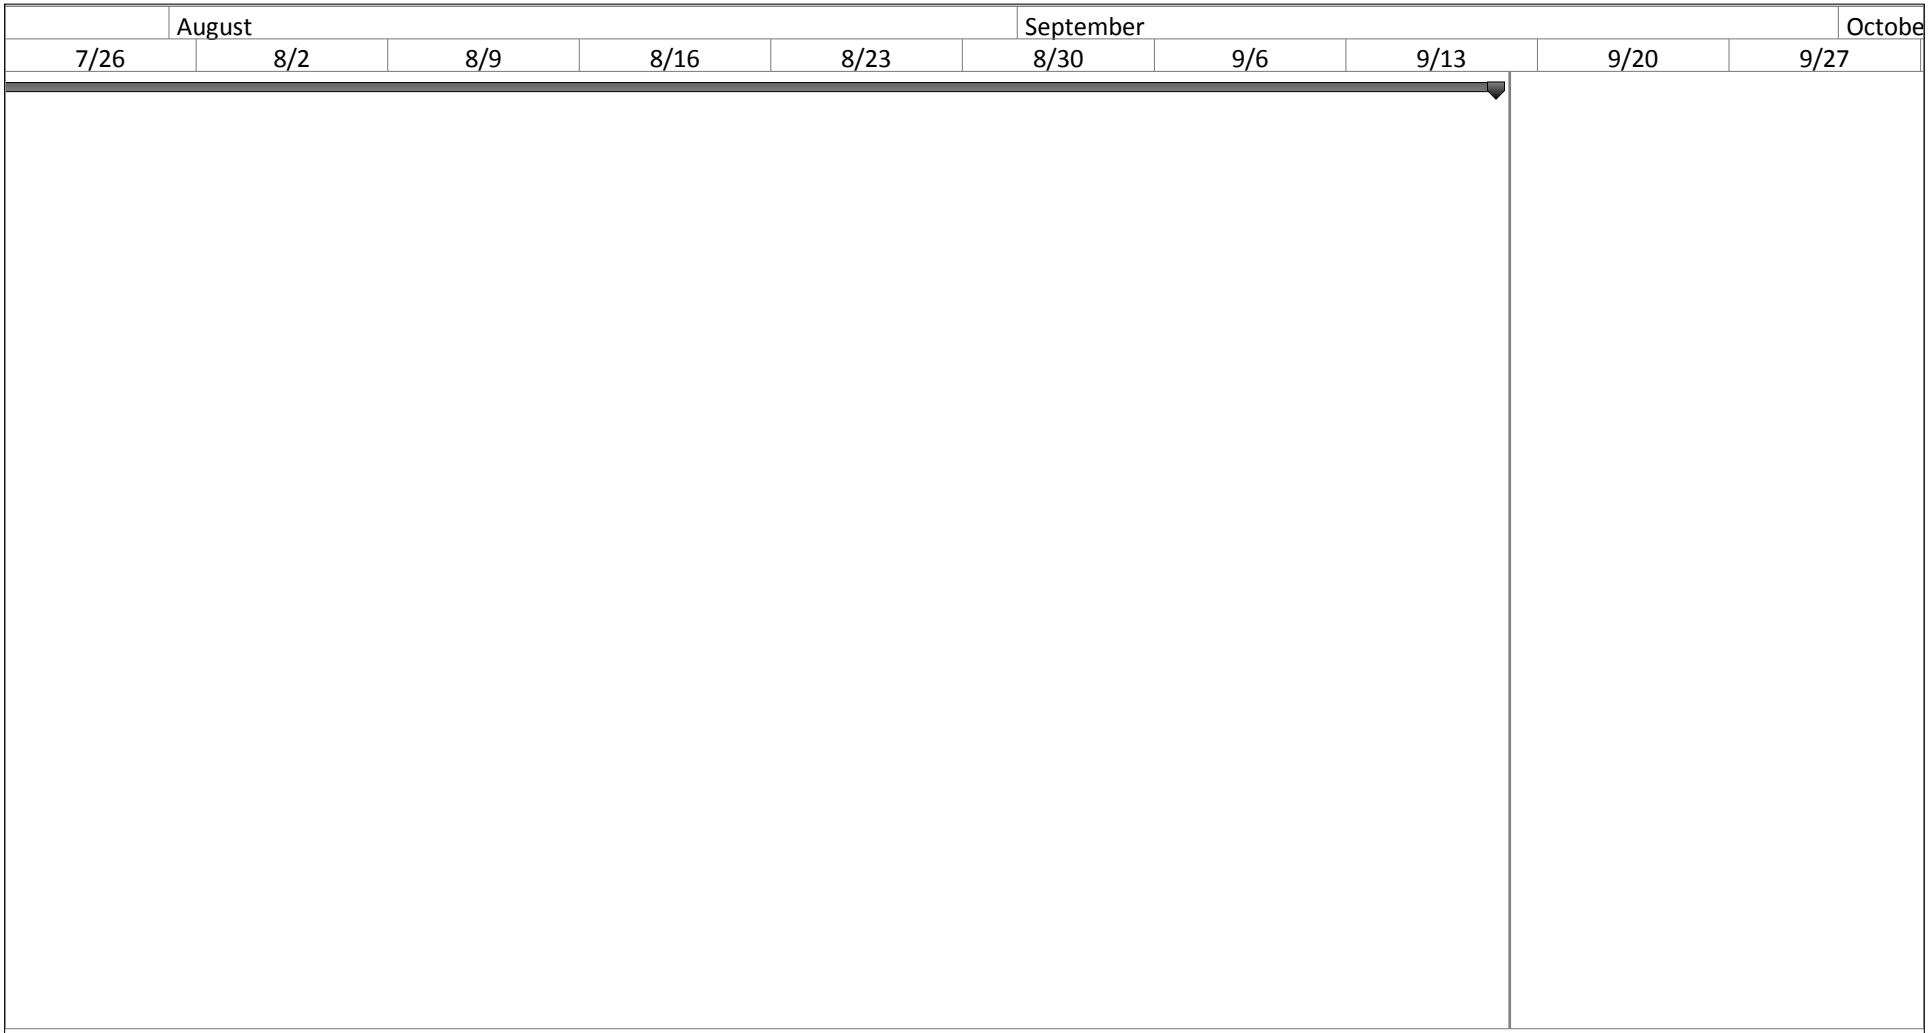

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

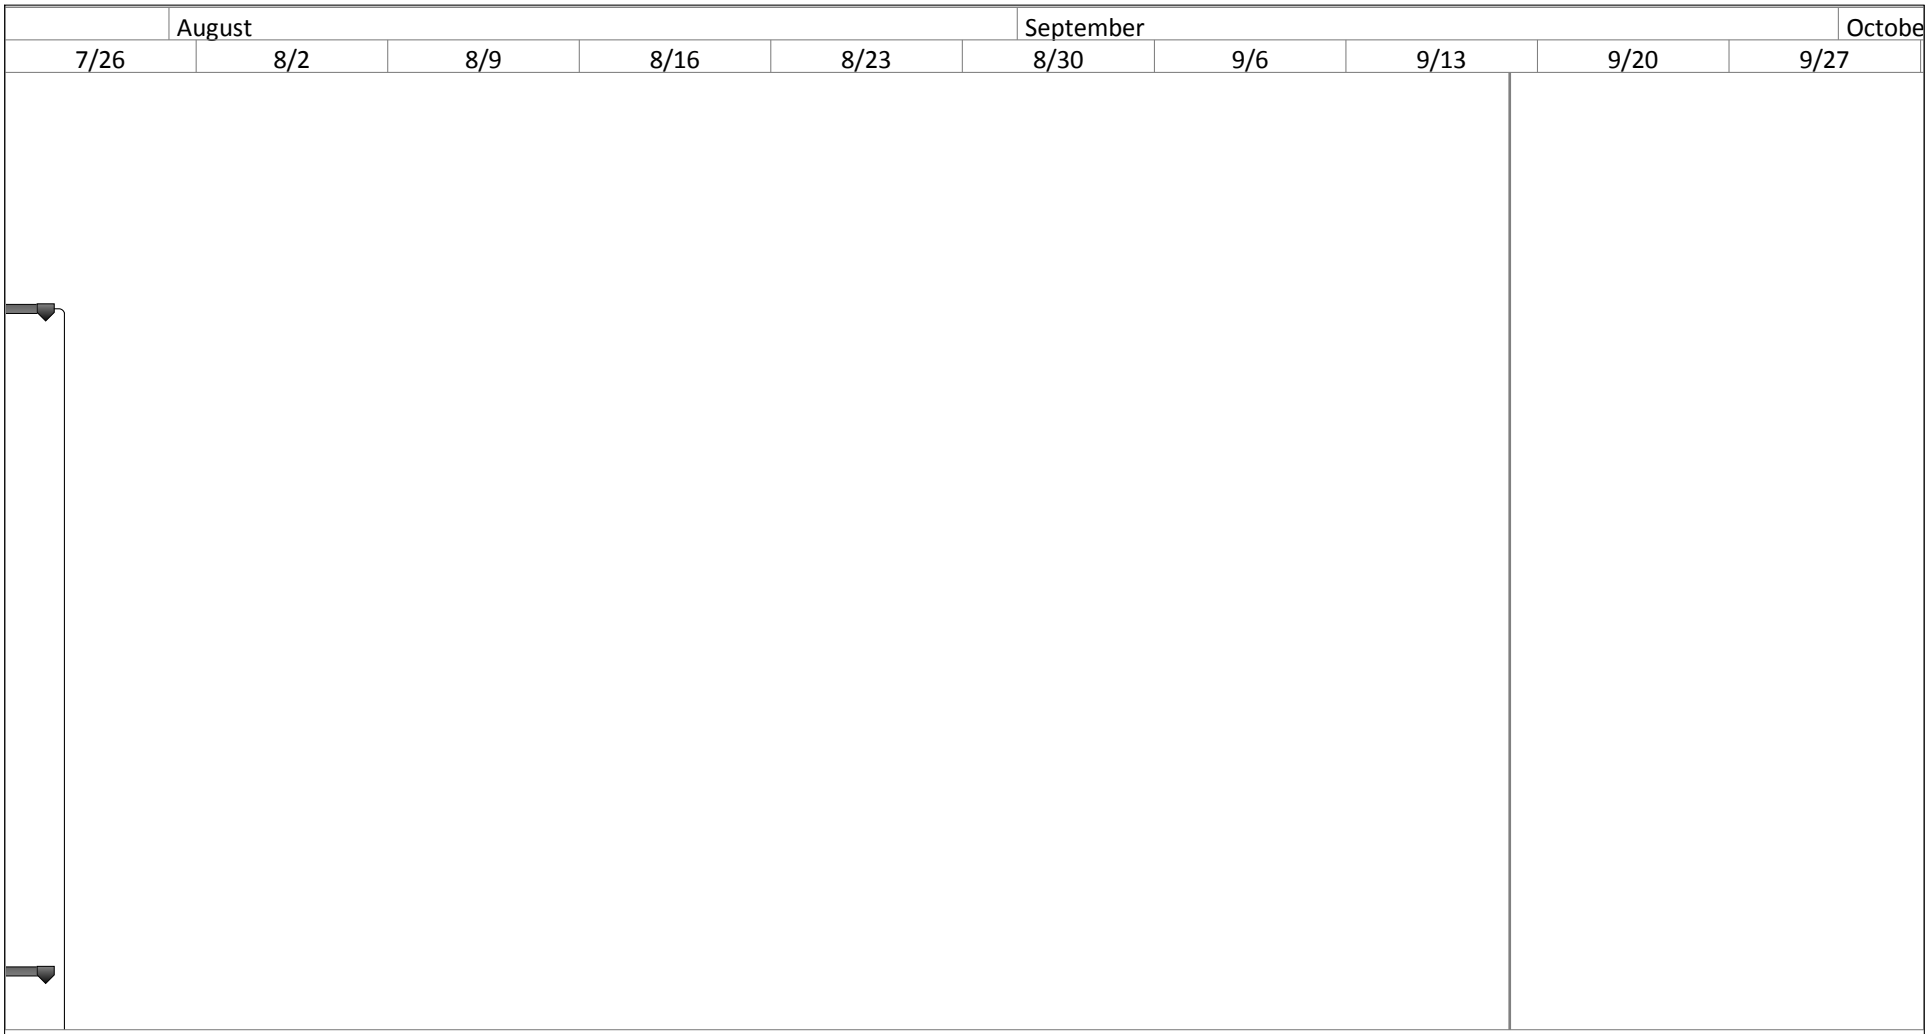

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

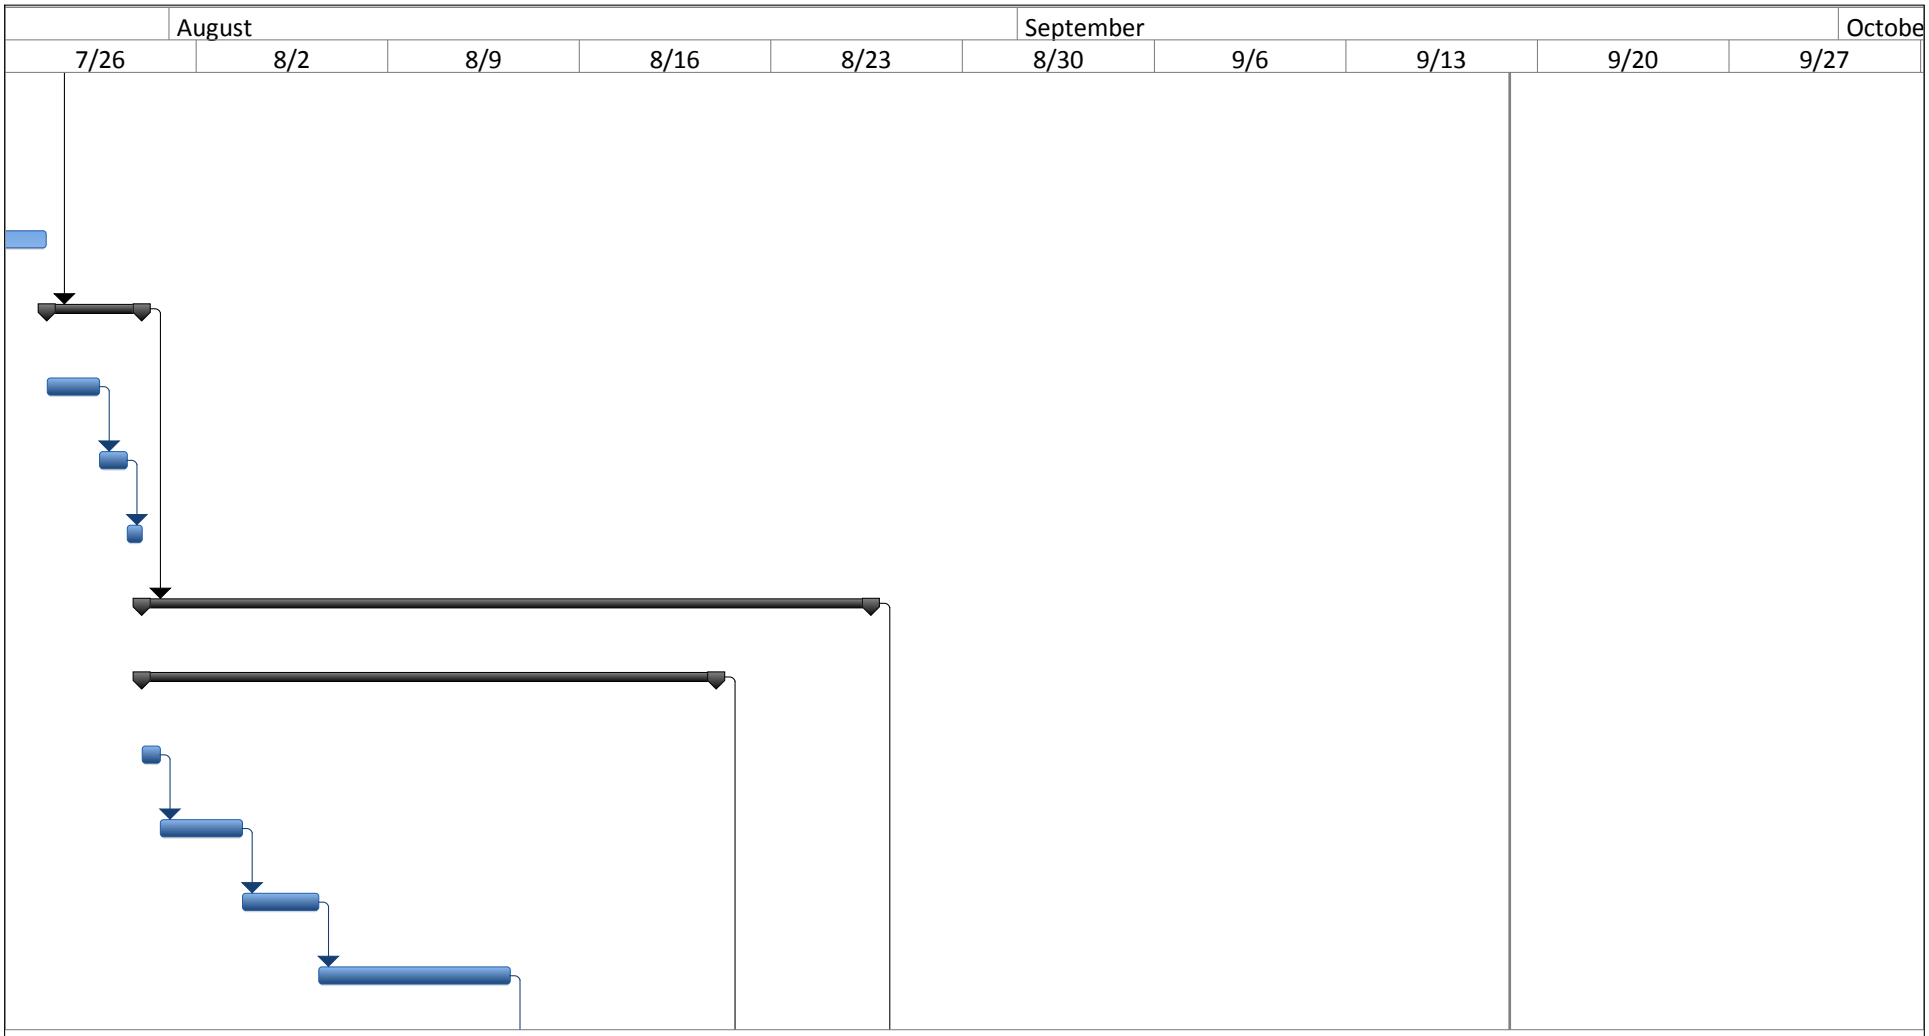

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

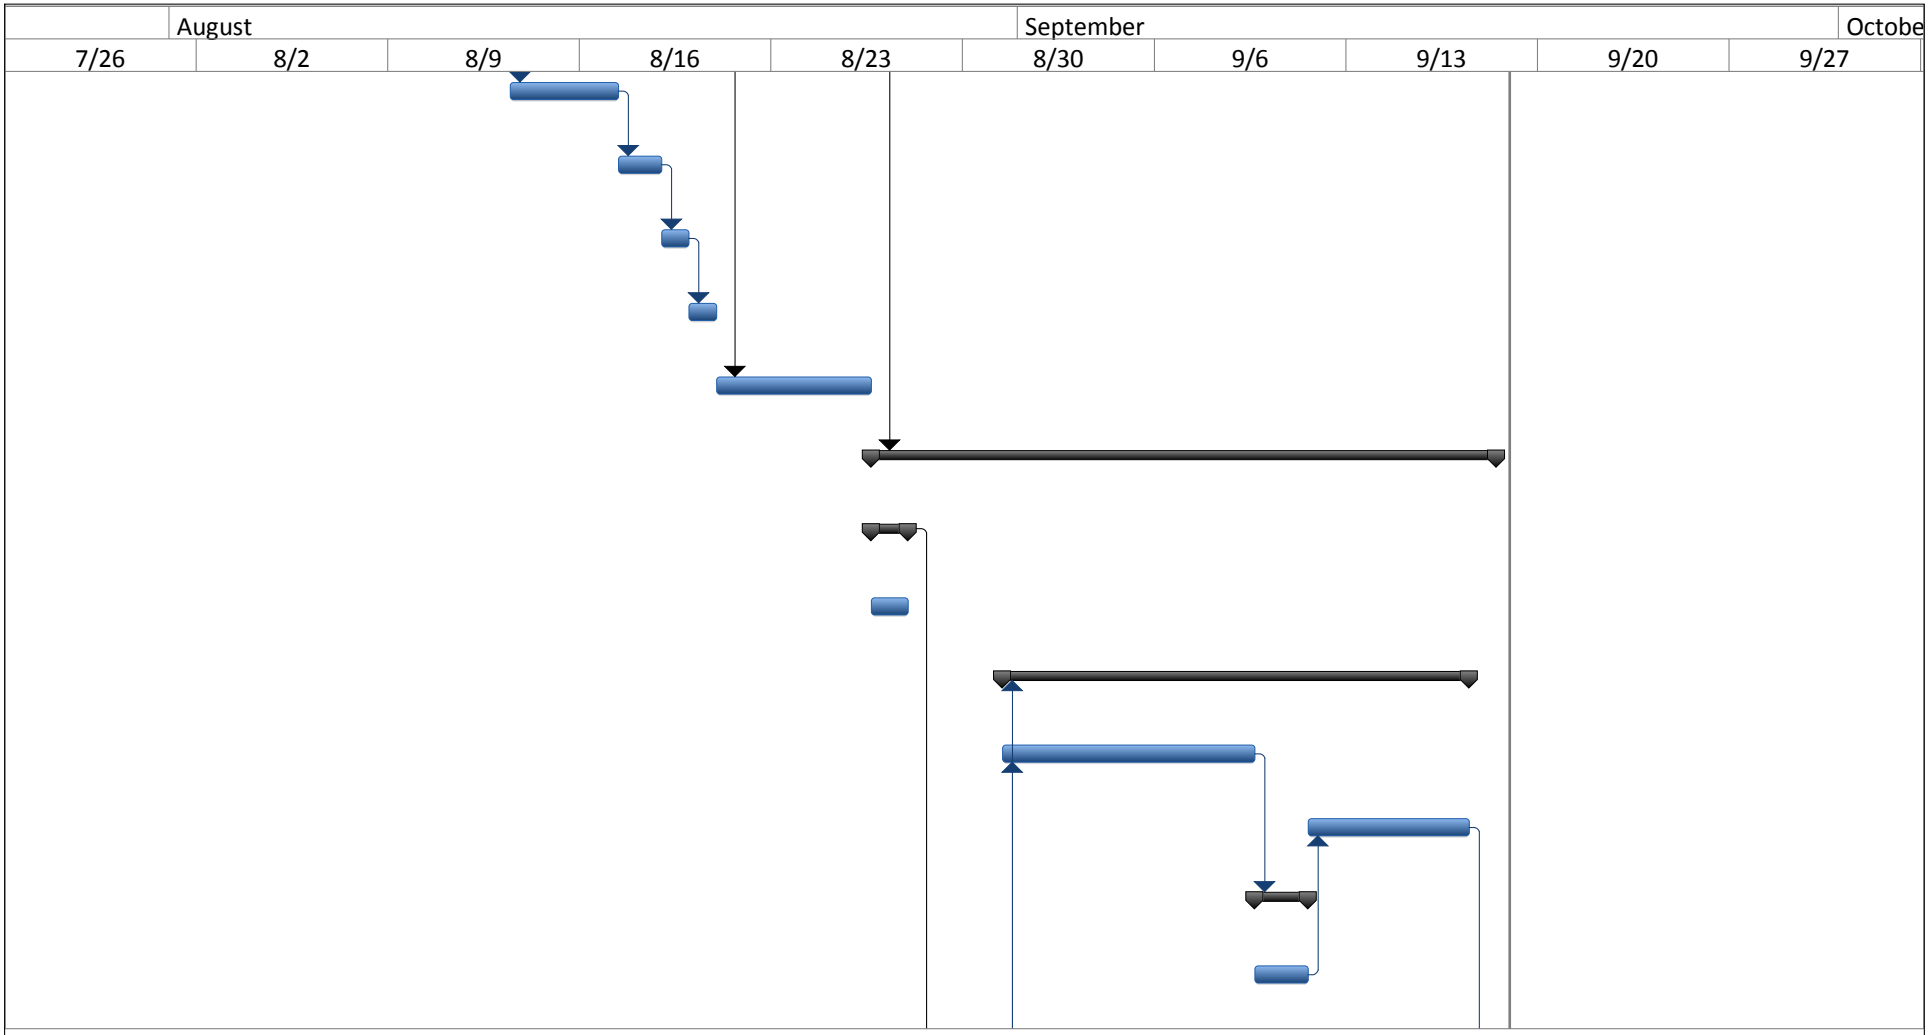

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

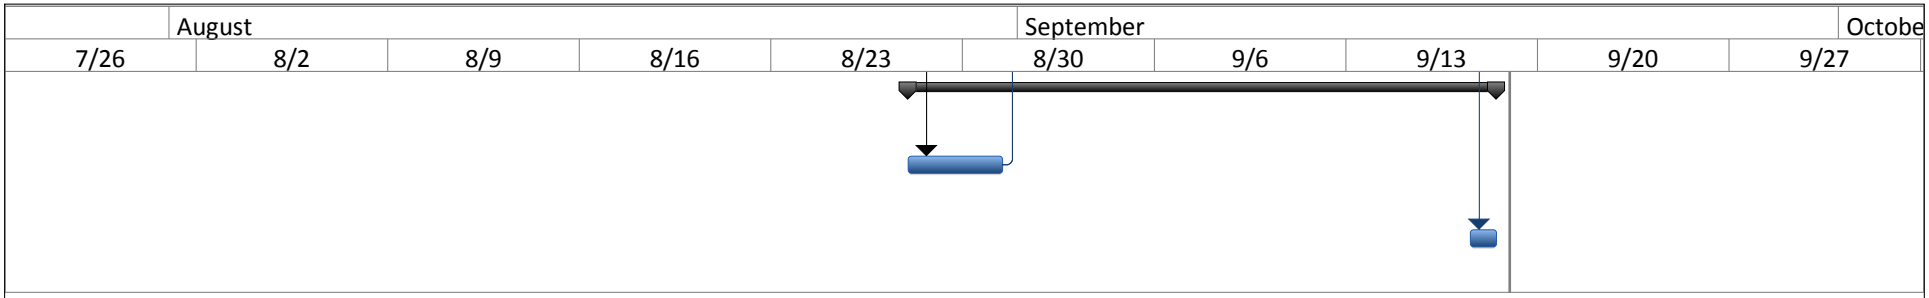

Project: Hardboard phase 1 1-2-15
Date: Fri 6/26/15

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
